

**Applied Geoscience and  
Technology Division (SOPAC)**

Private Mail Bag Suva  
Mead Road Nabua, Fiji Islands  
Telephone: (679) 3381377  
Fax: (679) 3370040/3384461  
www.sopac.org  
Email: director@sopac.org

**SPC Suva Regional Office**



SPC Headquarters  
BP D5  
98848 Noumea Cedex  
New Caledonia  
Telephone: +687 26 20 00  
Fax: +687 26 38 18

## **SPREP PACC COST BENEFIT ANALYSIS WORKSHOP: FOOD SECURITY PILOT DEMONSTRATION PROJECTS**

Suva, 24-27 January 2012

# **SIMPLE INTRODUCTION TO COST BENEFIT ANALYSIS**

Paula Holland  
Manager, Natural Resources Governance unit, Technical Support Services  
SOPAC Division  
Fiji Islands

## CONTENTS

1 INTRODUCTION.....	1
1.1 What is cost benefit analysis used for? .....	1
1.2 Broad steps .....	1
1.3 Why not use more conventional decision methods? .....	2
1.4 Financial feasibility versus economic feasibility.....	4
2 COST BENEFIT ANALYSIS AND THE PROJECT CYCLE.....	5
2.1 <i>Ex ante</i> cost benefit analysis .....	6
2.2 Mid project cost benefit analysis.....	8
2.3 <i>Ex post</i> cost benefit analysis .....	9
3 SOME CHALLENGES WITH COST BENEFIT ANALYSES .....	10
3.1 Data.....	10
3.2 Inputs.....	10
3.3 Selling the outputs .....	11
REFERENCES.....	11

## Annex

SELECTED EXAMPLES OF PACIFIC COST BENEFIT ANALYSES .....	13
----------------------------------------------------------	----

## 1 INTRODUCTION

Cost benefit analysis is a framework to assess the merits of an activity (project, policy) from the perspective of society (as opposed to a single individual). It involves:

- Measuring the gains and losses (benefits and costs) from an activity to the community using money as the measuring rod; and
- Aggregating those values of gains and losses and expressing them as net community gains or losses (see Pearce 1983).

### 1.1 What is cost benefit analysis used for?

Cost benefit analysis is used to help people make decisions. Depending on when the analysis is undertaken (before, during or after an activity), cost benefit analysis can provide information to help assess:

- whether a project or activity will be or is worthwhile:
  - Should we invest in this project?
  - Which of these two projects should we support?
    - .. Which project will give us the best pay off per dollar invested?
    - .. Which project will generate the highest value to society once we have paid for it?
- whether a project or activity has been worthwhile.

In the process of conducting a cost benefit analysis, the information generated may also inform:


- What it would take to make the potential benefits of an activity actually materialise (what the pre-conditions for success in the activity are);
- The progress of an activity and how it should proceed/be revised, based on the benefits and costs identified.

### 1.2 Broad steps

Cost benefit analysis involves comparing the values (costs and benefits) of an activity by assessing the benefits and costs faced by a community *with the activity* compared to *without the activity*. This allows decisions makers to see what difference the activity would make to well being. There are several basic steps involved in conducting a cost benefit analysis (Figure 1).

In some cases, step 1 of cost benefit analysis (defining options) may require little effort. This would be where activities (options) are pre-determined, such as where a community or government has already decided that an activity is important or where it appears to be the only option available. However, all other steps are critical to the analysis. Steps 2 and 3 generally require the most time, effort and expertise.

**Figure 1 Basic steps in a cost benefit analysis**

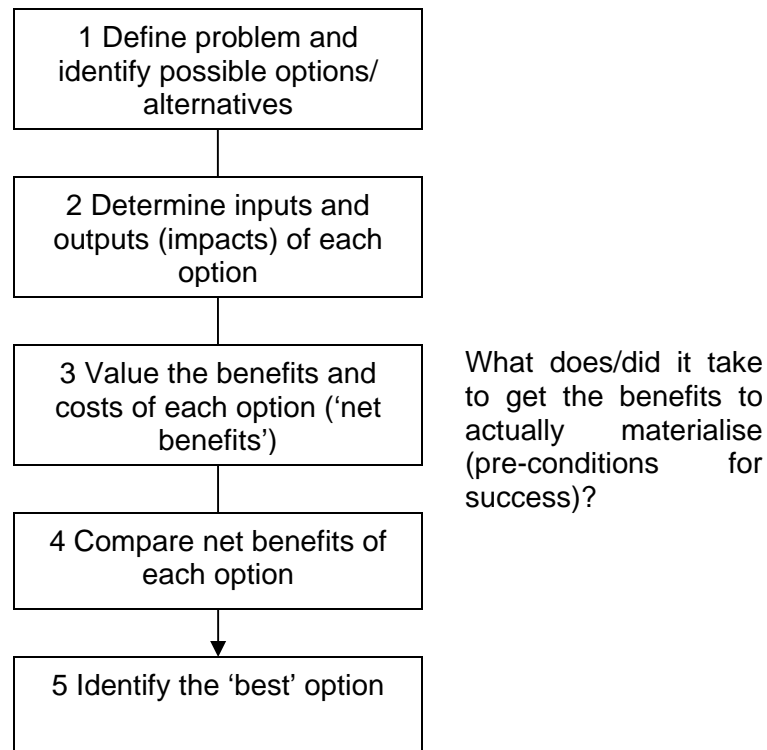

### 1.3 Why not use more conventional decision methods?

People can make decisions in several ways. In the Pacific, common ways to make decisions are:

- voting systems; and
- consensus.

Voting (democracy) draws on individuals' perceptions about the pros and cons of an activity. The activity with the highest votes 'wins' the right to proceed. Consensus based decision making focuses on different stakeholders reaching agreement on which activity to pursue (Lal and Holland 2010).

Compared to cost benefit analysis, both voting and consensus based decision making systems have limitations:

- Votes may bear little relation to the effect of the activity on human wellbeing (as measured by benefits and costs). Such a system is subject to political and emotive arguments.
- Consensus based decision making can be a time consuming and costly way to make decisions when many people are involved in the process. There can be

immense time and energy demands before people get to agree, especially where there are widely divergent opinions and or numerous groups are involved. In other words, consensus decision making can have high 'transaction' costs (Lal and Holland 2010).

Consider an intensive farming project that makes producers better off but which is expected to lead to run off and downstream pollution. As a result, those using the river for drinking water and washing might find the water no longer useable and might have to go further to find water or have to buy it. Using a voting system, votes on whether to back the project might appear like that in Table 1.

**Table 1 Vote based decisions versus economic benefit–cost analysis**

Stakeholder	Benefits (\$)	Costs (\$)	Net benefit (\$)	Vote
Farmers	15	10	5	1
Wholesalers	20	10	10	1
Retailers	15	10	5	1
Water consumers	20	40	-20	-1
Environmental group	10	20	-10	-1
Total social impacts	80	90	-10	-1

Source: Lal and Holland 2010.

Assuming these impacts, three groups might be expected to vote in favour of the project while two would reject it. Using a vote based or democratic system, the project would be supported regardless of its overall negative impacts. Under a consensus system, deciding whether or not to support the project would be expected to lead to considerable debate and would likely consume a large amount of time and – possibly – resources.

By comparison, a cost benefit analysis would explicitly include consideration of the likely benefits and costs the project would involve. If the benefits and costs of the project using to the different stakeholders were considered and summed, it could be seen that – overall – the total benefits of the project would likely be outweighed by its costs. That is, the community would be less well off if the project went ahead.

Consider now if the project still caused run off and downstream pollution but the food production benefits were considerably higher. In this case, impacts and resulting decisions might look like that provided in Table 2.

In this case, consideration of the likely benefits and costs would suggest that – overall – the total benefits of the project outweigh its costs. That is, the community as a whole might be better off if the project went ahead. On the other hand, the analysis would still highlight that the project would be expected to have negative impacts on water quality and the environment. If the project went ahead, expectation of these negative impacts might result in resistance to the project from community groups and obstruct project success. Identifying the distribution of benefits and costs should then form part of the

dialogue for how best to design the project to minimise impacts and decide whether the project is indeed appropriate.

**Table 2 Vote based decisions versus economic benefit–cost analysis**

Stakeholder	Benefits (\$)	Costs (\$)	Net benefit (\$)	Vote
Farmers	25	10	15	1
Wholesalers	25	10	15	1
Retailers	20	10	10	1
Water consumers	20	40	-20	-1
Environmental group	10	20	-10	-1
Total social impacts	100	90	10	1

The advantage of using a cost-benefit framework is therefore that decision makers are forced to consider the *overall impact* of projects from the perspective of the group. It also allows for decision makers to view the *distribution* of benefits and costs across the community. Using this information, more informed decisions can be made.

Importantly, cost benefit analysis is not the only way to make a decision. The findings of an analysis can then be used to *inform* voting and consensus processes so that people make more balanced decisions.

#### 1.4 Financial feasibility versus economic feasibility

Note that the examples provided describe the *benefits* and *costs* of activities, as distinct from their *revenues* and *costs*. Cost benefit analysis describes the merits of an activity from *society's* perspective – so it considers all impacts. By comparison, a financial feasibility assessment would consider only the financial impacts of an activity and would not include impacts that do not involve money, such as environmental impacts, the distribution of wealth impacts across the community or effects on social cohesion.

For example, section 2.1 describes a cost benefit analysis in Kiribati where it is found that dredging a lagoon for sand is commercially feasible. By comparison, the cost benefit analysis also conducted indicates that the project would financially disadvantage certain groups in the local community. That is, even though the project would make a small profits, the benefits and costs experienced by different groups would be unevenly distributed across the community. This could ultimately lead to the failure of the project. As a result, the project would need to be redesigned to minimise these risks.

A major activity that would affect both incomes as well as changes in how resources are used might thus require both a financial feasibility assessment as well as a cost benefit analysis.


## 2 COST BENEFIT ANALYSIS AND THE PROJECT CYCLE

Cost benefit analysis can be undertaken at any stage in the life of a project. They may occur:

- Before an activity (*ex ante*) to decide whether or not to undertake an activity and or to identify key topics (variables) to monitor to check that the activity is on track;
- During an activity to inform the progress of an activity and enable its refinement as needed to maximise benefits;
- Following an activity (*ex post*) to assess whether or by how much an activity improved the quality of life (Figure 2).

Critically, *ex ante* and in-project assessments can help inform what is needed to ensure that the potential benefits of an activity actually materialise (to identify the pre-conditions for project success).

**Figure 2 Cost benefit analysis in the project cycle**

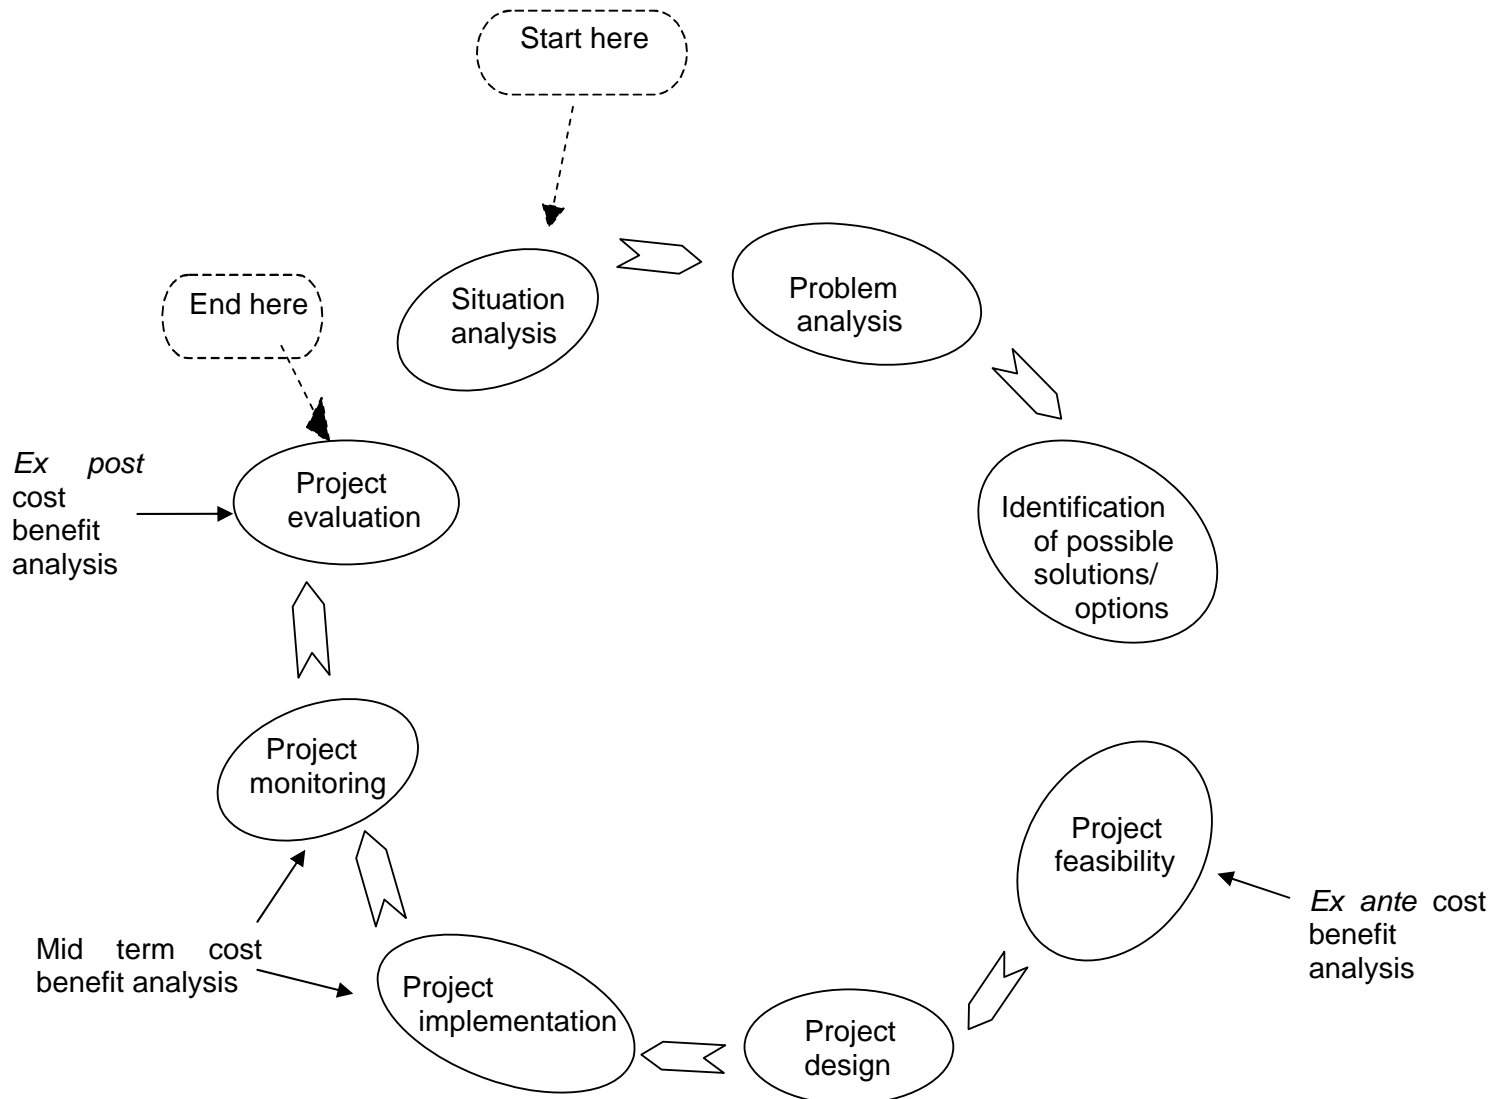

In the Pacific, the use of cost benefit analysis to support the design and assessment of projects is still relatively new. 10 years ago, examples of cost benefit analysis were hard to find. A good example of a project that did draw on the lessons of cost benefit analysis to inform which activities to fund is the SPREP-executed South Pacific Biodiversity Conservation Project (SPBCP). Otherwise, however, cost benefit analyses were generally limited in application (or at least, limited in documentation and accessibility).

By comparison, there has been a relative explosion in the number of cost benefit analysis used in recent years (see Annex for some examples).

## **2.1 *Ex ante* cost benefit analysis**

The following case study summary is taken from Greer (2007). In Kiribati, a combination of growing populations, inward migration from rural areas/islands and development investment has resulted in the rapid growth of its capital, located on the small atoll of Tarawa. Growth has been typified by an increase in small scale domestic developments (such as houses) as well as sporadic large scale investments (such as public facilities such as hospitals, schools and or government buildings). The construction to underpin these developments demands access to ‘aggregates’ – sand, gravel, rip rap or rocks used for construction.

Conventionally demand for aggregates for construction around Tarawa has been met by digging up aggregate from the beaches and coastal flats. Although this mining is a cheap and effective way to supply aggregates on Tarawa, the supply is often insufficient to meet local demand. Moreover, the removal of too much aggregate on Pacific atolls has been demonstrated to increase coastal erosion. (See Webb 2005a, 2005b, 2006.) On Tarawa, increased flooding of key amenities such as the hospital, and saltwater intrusion to ground water has thus been linked to the coastal mining. Flooding is becoming an increasing concern in the face of rising sea levels from climate change. At a time when Tarawa residents most need aggregates to build seawalls to protect them from the sea, removing aggregates from their coastlines to build those walls ironically puts them at greater risk of flooding.

An alternative to coastal mining is to import aggregate from overseas (with Fiji being a common source for the Pacific). However, importation of aggregate is usually extremely expensive, out of the reach of most commercial or domestic users and therefore only practical for donor led developments. Further, importation risks the introduction of plant, insect or other pests. Previous imports to Pacific atolls countries had seen the discovery of a (dead) frog in cargo to Kiribati (see Greer 2007) and the introduction of some 19 invasive weed species to Tuvalu (see Ambroz 2009).

Given the risks to the environment of importing aggregate and the threats to wellbeing from coastal mining, the Government of Kiribati sought to replace aggregates sourced from the beaches with aggregates located on the sea bed of Tarawa lagoon. Work conducted under a previous development projects had confirmed the existence of large reserves of aggregate there and assessed their suitability for low scale construction or infilling (Smith and Biribo 1995). Theoretically, these aggregates could be extracted from



the lagoon bed by using a suction dredge (effectively sucking aggregates from the seabed using a pipe) or clamshell dredge (scraping them up from the seafloor) attached to a barge. The aggregates could then be transferred to shore for sorting and use. If dredging aggregates could continually replace coastal mining, coastal protection could be increased and livelihoods improved. However, the Government of Kiribati was keen that any activity to access aggregates in an ongoing manner would be financial and socially sustainable. An economic analysis of dredging was therefore conducted to assess this.

Based on a provisional design for a suction dredge in Tarawa lagoon, preliminary analysis indicated that lagoon dredging could be commercially feasible in a 'quiet' year when no major developments were underway and only demand as usual applied. In these cases, a small profit (around A\$60 000) might be expected. In years when large scale developments were also underway, it was estimated that profitability might be expected to improve. From an economic perspective, lagoon dredging was estimated to generate potential economic returns of 16 per cent. This high rate of return does not include the positive benefits of protecting infrastructure and property, public utilities (water and sewerage, electricity and phone lines), agriculture and public health. These benefits were not quantified because of lack of data on the impact of coastal mining (as distinct from natural processes) on coastal process. However, they could be significant. The economic return from diverting aggregate mining from the coasts to the lagoon is therefore likely to be higher than 16 per cent in real terms.

Although the financial and economic benefits of lagoon dredging looked promising, there were a number of issues that threaten its sustainability. Critically, a recent household survey had indicated that around 1200 local families conducted coastal mining and at least 150 relied on the sale of those aggregates as their primary source of income (Pelesikoti 2007). Commercial dredging would compete for business against these households as well as against commercial miners to sell its sand and gravel. The risk is that – especially where families rely on the sale of coastal aggregates for income – businesses and households could undercut the sale price of lagoon sourced aggregates. The results would be continuing coastal mining, continued coastal erosion and the waste of resources involved in establishing a dredge operation that would not survive.

In light of these drivers, economic analysis indicates a number of policy implications to prevent coastal erosion including:

- a total ban on coastal mining would be impractical. If current restrictions are not observed, it is unlikely that the government could enforce a wider ban. It would be more sensible to rework the current designated/non designated area scheme and police that more effectively, accompanied by an awareness campaign;
- A strategic communications campaign would be needed before embarking upon operations to ensure that the community understands the benefits of controlling coastal mining and the benefits of using lagoon sourced aggregates instead;
- A sensitive and sensible scheme would be required to assist disenfranchised families to cope with the loss of income generation from coastal mining. The government will need to embark on community consultations to identify options.

Other critical issues affecting the feasibility were the need to consider dual pricing policies (to encourage purchases from the company rather than from local coastal miners) and the need for an appropriate environmental impact assessment and ongoing environmental monitoring.

The findings of the analysis were ultimately incorporated by the Government of Kiribati to a proposal fund the establishment of commercial dredge operations to divert aggregates sourcing to Tarawa lagoon. The proposal was successful and the EU provided €2.2 million to establish a dredge company over two years and ultimately transfer its operation to the Government. The project is presently involved in intensive consultations with the community on a plan for community involvement in the scheme and the dredge is being built as we speak.

## **2.2 Mid project cost benefit analysis**

The following case study summary is taken from taken from Woodruff (2008). River floods, especially severe flash floods caused by heavy rainfall, are a frequent occurrence in Apia, Samoa, during the rainy season due to its geography and high rainfall. Apia, the capital, is built on the low-lying floodplains of five rivers: the Fagali'i to the east, and the Fulouasou, Gasegase, Mulivai and Vaisigano to the west (Taule'alo 2002). Severe floods have occurred in Apia in 1939, 1974, 1990, 2001 and 2006. The Government of Samoa recently worked with international agencies in the mid 2000s to develop management guidelines and a plan of action to reduce flood risks in the lower Vaisigano catchment area. The initial Action Plan included a number of structural options and non-structural management options that could potentially reduce flood risk:

- Structural flood management options:
  - Construction of floodwalls
  - Construction of a by-pass channel
  - Construction of a reservoir
  - Increasing channel conveyance
  - Pumping
  - River maintenance
- Non structural flood management options:
  - Development control- raised floor heights
  - Improved flood forecasting system

The activities considered in the plan included investment in surveillance and forecasting. This was important given that Apia is a well established city and that people and businesses are unlikely to relocate, despite the ongoing risk of flooding. Consequently, up front investment may be appropriate to enable forecasting so that people can plan for and mitigate disaster impacts.

The options contained in the plan were numerous. A preliminary cost benefits analysis was conducted of a selection of measures to assist the Government of Samoa compare options and select which measures to target.

The results (Woodruff 2008) indicated that while investing in structural flood management options was unlikely to be economically viable due to high construction and maintenance costs, the economic pay-off from investing in non-structural measures including raised floor heights might be very high. For example, for every Tala invested in constructing homes with elevated floor heights, it was estimated that 2 to 44 Tala would be saved in terms of avoided flood damages. Similarly, the benefits from investing in an improved flood forecasting system were found to be positive, with every Tala invested in the improved system estimated to yield between 1.72 to 1.92 Tala in avoided future flood damages.

The findings of the study were intended to be used to implement the Samoa Flood Management Action Plan and, importantly, to lobby the government to invest in disaster mitigation measures such as more training in flood forecasting and building controls to raise floor levels. Some donors expressed interest at the time the report was released in supporting some of the interventions that were assessed as most economically feasible. For example, the European Union expressed early interest in using the information generated to determine whether to invest in further flood modelling work (Nadia Meredith, European Union Water Sector Support Programme, personal communication, 11 September, 2007). It is unclear at this point whether investment was finally secured.

### **2.3 Ex post cost benefit analysis**

The following case study summary is taken from Woodruff (2007). The coconut tree is a vital component of island ecosystems and economies, and traditionally copra has been an important source of rural income on many of Pacific islands. Although the technology has been around for many years, it has only been in the last ten years, that there has been renewed interest in using coconut oil as a biofuel in the Pacific (Cloin 2005). The development of coconut oil as a renewable energy in the region not only provides the opportunity to reduce reliance on imported fossil fuels but also to provide rural communities with a cost effective source of energy.

In order to promote rural electrification and sustainable livelihoods, and demonstrate the use of biofuel as a substitute for diesel, the Fiji Department of Energy, with support from the Secretariat of the Pacific Community and the French Government, installed specially adapted generators, designed to operate on pure coconut oil, in Welagi Village located on Taveuni Island in 2001, and in Sawana Village, located on the island of Vanua Balavu, in the Northern Lau group, in 2000 (Courty 2000). Village committees are responsible for overseeing the operation and maintenance of the generators, as well as setting and collecting user fees in order to ensure that the projects are financially sustainable (Fiji Department of Energy 2001).

A preliminary economic assessment of the projects indicated that, in Vanua Balavu, given high transport costs, locally produced coconut oil enjoyed a clear price advantage compared with imported diesel fuel. However, the coconut oil mill on the island, which was intended to supply the project with biofuel had ceased operations, and a local source of coconut oil is no longer available. For a brief period, coconut oil was shipped

to the project site from another mill. However, added transport costs meant that using coconut oil in the generator was more costly than diesel fuel (Khan 2005).

In Welagi, the price advantage of biofuel compared with diesel fuel turned out to be less clear-cut since diesel fuel transport costs from the main port of Suva were lower. Also, the Welagi generator was operating on diesel fuel since there is a limited local supply of coconut oil. Ideally, the community could have switched between fuels, depending on which fuel is least cost. Therefore, the results from the analysis indicated that, for coconut biofuel to provide the least-cost option for rural electrification, compared with diesel fuel, there needed to have been sufficient low-cost coconut oil resources available locally, and households should have been located in a location remote enough that added diesel fuel shipping costs were sufficiently high to make locally produced coconut oil cost competitive.

### **3 SOME CHALLENGES WITH COST BENEFIT ANALYSES**

#### **3.1 Data**

Information is needed in a cost benefit analysis to assess benefits and costs. In general, the financial costs of a proposed activity are relatively easy to determine. More difficult is the estimation of benefits or intangible costs. This is because the benefits of many activities – especially before a project takes place – are still only hypothetical so their true extent may not be clear.

Predicting the impacts of a project cannot be achieved unless the situation without project is understood. Take the recent assessment of water projects in Tuvalu, for example (Gerber et al 2011). In this assessment, three projects were executed to improve the quality of water on Funafuti. In so doing, the projects were expected to reduce the level of water borne disease arising from consuming presently contaminated water. Unfortunately, while the Department of Health was able to provide data on the incidence of illnesses that *might* be caused by poor water (such as diarrhoea or boils), officials were unable to establish what percentage of those cases were actually caused by poor water consumption compared to – say – poor sanitary practices (such as leaving food out of the fridge for too long, not washing hands after using the bathroom etc.) (See Gerber et al. 2011.) In the absence of basic information on how many people suffer from water borne disease, assessing the impact of a project to address is difficult.

Even if such data exists and the physical impacts of projects can be determined, it can be difficult to assign a monetary value to the non financial impacts of some projects. Numerous techniques exist to do this (see Pearce 1983) and they are evolving continually. Nevertheless, challenges exist for each.

#### **3.2 Inputs**

Conducting a cost benefit analysis will take time and expertise. Data may need to be bought. Travel may need to be conducted. All of these items cost. In particular, there are only a limited number of agencies in the Pacific that routinely conduct economic analysis

of development projects that link with the natural environment. As a result, it may be difficult to find the necessary expertise to conduct the work. Alternatively, it may be expensive to do so if consultants are used. There is a need to build the expertise of national agencies to conduct economic analysis for the development of Pacific island countries.

### **3.3 Selling the outputs**

Cost benefit analysis is a compelling input to the decision making process. By highlighting the economic impacts of projects, decision makers have a valuable insight to the contribution that different activities can make to social well being. Nevertheless, economic issues are not the only consideration in a decision. For example:

- projects must be socially acceptable. A project which offers substantial net benefits but which disadvantages key stakeholders in the process is likely to be culturally unacceptable and or politically difficult to sell;
- a project that offers a relatively poor pay off may nevertheless be important to support for non economic reasons such as to prevent social break down or to ensure continuity and trust.

The economic value of an activity thus needs to be considered in the context of other critical issues including, for example, the sustainability of project impacts, environmental impacts, cultural impacts and the distribution of wealth (equity). As indicated, economic considerations can feed into the decision making process (such as voting or consensus) but would be unlikely to be the sole determinant of whether an activity should be/ should have been pursued.

### **REFERENCES**

Ambroz, A. 2009. An Economic Feasibility Assessment of Lagoon Dredging in Funafuti, Tuvalu, EU EDF 8 – SOPAC Project Report, August.

Cloin, J. 2005. Coconut Oil as a Biofuel in Pacific Islands: Challenges and Opportunities. SOPAC Miscellaneous Report 592. SOPAC Secretariat, Suva.

Courty, P. 2000. Copra Biofuel for a Sustainable Decentralised Rural Electrification. Presentation made at 9<sup>th</sup> PPA Conference and Trade Exhibition, 21<sup>st</sup>-24<sup>th</sup> August 2000, Brisbane.

Fiji Department of Energy 2001. Memorandum of Understanding between the Department of Energy and Welagi Villagers.

Greer Consulting Services 2007. Economic Analysis of Aggregate Mining on Tarawa, EU SOPAC Report 71.

Khan, I. 2005. Biofuels in Fiji: Socio-Economic and Technical Constraints and Opportunities through Experiences in Welagi and Lomaloma". Paper presented at PPA Workshop, Nadi. 17<sup>th</sup> November 2005.

Pearce, D. 1983, *Cost benefit Analysis*, 2<sup>nd</sup> edition, Macmillan, London.

Pelesikoti, N. 2007. Extent of Household Aggregate Mining in South Tarawa, EU EDF8/9 – Project Report ER0072, SOPAC.

Smith, R. and Biribo, N. 1995. Marine Aggregate Resources Tarawa Lagoon, Kiribati - Including Current Meter Studies at Three Localities, September, SOPAC Technical Report 217.

Taule'alo, T. 2002. Planning for Sustainable Drainage and Sewerage Services in Apia, Pacific Economic Cooperation Council, Report prepared for Sustainable Cities Taskforce Seminar 4<sup>th</sup> and 5<sup>th</sup> November 2002, Noumea.

Webb, A. 2005a. Technical Report – An Assessment of Coastal Processes, Impacts, Erosion Mitigation Options and Beach Mining Bairiki/Nanikai Causeway, Tungaru Central Hospital Coastline and Bonriki Runway – South Tarawa, Kiribati. EU EDF 8/9 – SOPAC Project Report 46.

Webb, A. 2005b. Tuvalu: Technical and Country Mission Report: Assessment of Aggregate Supply, Pond and Lagoon Water Quality & Causeway Construction on Funafuti and Vaitupu Atolls. EU EDF 8/9 – SOPAC Project Report 36.

Webb, A. 2006. Tuvalu Technical Report: Coastal Change Analysis Using Multi-Temporal Image Comparisons – Funafuti Atolls. EU EDF 8/9 – SOPAC Project Report 54.

Woodruff, A. 2007. An economic assessment of renewable energy options for rural electrification in Pacific Island Countries, SOPAC Technical Report 397.

Woodruff, A. 2008. Economic analysis of flood management in the lower Vaisigano catchment area, EU EDF – SOPAC Project Report 69g.

## SELECTED EXAMPLES OF PACIFIC COST BENEFIT ANALYSES

Study	Topic	Country	Year
McKenzie 2004	Investments in the black pearl industry	Tonga	2004
Pesce et al. 2004	Investments in sustainable forestry (certification)	RMI	2004
Greer 2005	Investment in a bridge for rural development	PNG	2005
Lal et al. 2005	Costs of coral reef extraction	Fiji	2005
Lal et al. 2006	Investments in liquid waste management	Tuvalu	2006
McKenzie et al. 2006	Costs of erosion from coastal mining	Cook Islands	2006
Greer 2007	Prevention of coastal erosion	Kiribati	2007
Woodruff 2007	Investments in renewable energy	Niue	2007
Zieroth et al. 2007	Biofuel from coconut resources	Samoa	2007
Holland 2008	Benefits of flood warning	Fiji	2008
Woodruff 2008	Benefits of flood intervention	Samoa	2008
Ambroz 2009	Benefits of coastal protection	Tuvalu	2009
Ambroz 2010	Least cost analysis of water supply options	Niue	2010
Gerber 2010	Economic assessment of water safety planning	Palau	2010
Gerber 2011	Economic assessment of IWRM	RMI	2011
Gerber et al. 2011	Economic assessment of water improvements to adapt to climate change	Tuvalu	2011
Talagi 2011	Economic assessment of water safety planning	Solomon Islands	2011

### References

Ambroz, A. 2010. Niue Technical Report: Least-cost analysis of water supply options in Niue. SOPAC Technical Report.

Gerber, K. 2010. An Economic Assessment of Drinking Water Safety Planning Koror-Airai, Palau, SOPAC Technical Report 440, Fiji.

Gerber, F. 2011. A preliminary economic assessment of integrated water resources management: Laura, Republic of the Marshall Islands, SOPAC.

Gerber, F., Holland, P. and Lal, P. 2011. The DCCEE-IUCN Project: Assessing the Social and Economic Value of Climate Change Adaptation in the Pacific Region: Case Study: Water Quality, Quantity and Sanitation Improvements as an Adaptation to Climate Change, Tuvalu – A Preliminary Assessment, IUCN, Fiji.

Greer Consulting Services 2005. Economic Analysis of Botue Bridge, Final Report to the AusAID-funded PNG Incentive Fund.

Greer Consulting Services 2007. Economic Analysis of Aggregate Mining on Tarawa, EU SOPAC Report 71.

Holland, P. 2008. An economic analysis of flood warning in Navua, EU-SOPAC Project Report 122, Fiji.

Lal, P. and Cerelala, A. 2005. Financial and Economic Analysis of Wild Harvest and Cultured Live Coral and Live Rock in Fiji, A Report prepared for the Foundation of the Peoples of the South Pacific International, Republic of Fiji Islands, the South Pacific Regional Environment Programme, Samoa and the Department of Environment, Ministry of Lands and Mineral Resources, Republic of Fiji Islands, August ([http://www.fspi.org.fj/Publications/Coastal/Socio-economic\\_analysis\\_aquarium\\_coral-Fiji.pdf](http://www.fspi.org.fj/Publications/Coastal/Socio-economic_analysis_aquarium_coral-Fiji.pdf) accessed 27 September 2007).

Lal, P. and Fakau, L. 2006. Economics of Waste Management in Tonga. A report prepared for the Tongan Government and IWP SPREP, Suva, Nukualofa and Apia.

Lal, P. and Holland, P. 2010. 'Integrating Economics into Resource and Environmental Management: Some recent experiences in the Pacific,' IUCN: Gland, Switzerland and Suva.

McKenzie, E. 2004. A cost-benefit analysis of projects implemented to assist the black pearl industry in Manihiki Lagoon, Cook Islands, TR0371.

McKenzie, E., Woodruff, A. and McClennen, C. 2006. Economic assessment of the true costs of aggregate mining in Majuro Atoll, Republic of the Marshall Islands, TR0383.  
Pearce, D. 1983, Cost benefit Analysis, 2nd edition, Macmillan, London.

Pesce, F. and Lal, P. 2004. "The profitability of forest certification in tropic hardwood plantation: a case study of the Kolambagarra Forest Products Ltd. from the Solomon Islands." Economic Management and Development, Crawford School of Economics and Government, EMD Discussion Paper 5, Canberra.

Talagi, D. 2011. An Economic Assessment of Water Safety Planning: Niue, SOPAC Technical Report 443.

Woodruff, A. 2007. An economic assessment of renewable energy options for rural electrification in Pacific Island Countries, SOPAC Technical Report 397.

Woodruff, A. 2008. Economic analysis of flood management in the lower Vaisigano catchment area, EU EDF – SOPAC Project Report 69g.

Zieroth, G., Gaunavinaka, L. and Forstreuter, W. 2007. Biofuel from Coconut Resources in Rotuma: A Feasibility Study on the Establishment of an Electrification Scheme using local Energy Resources, PIEPSAP, SOPAC, Fiji.
